

News Bulletin

ISG

Issue 8 – May 2015

Programme Update


Since our last Bulletin was issued we have continued to make excellent progress with the works on site.



The concrete frame to the Art building is progressing well. The 2nd floor slab is currently being installed, with the ground floor & first floor walls and columns completed between March through to the start of April.

We are pleased to announce that we have completed the removal of earth from site, with a total of 28,345 tonnes excavated. This results in a significant reduction in the vehicle movements on the local roads.

The swimming pool structure works has now commenced and the concrete structure to the fitness/dance studio area has continued to progress well also.

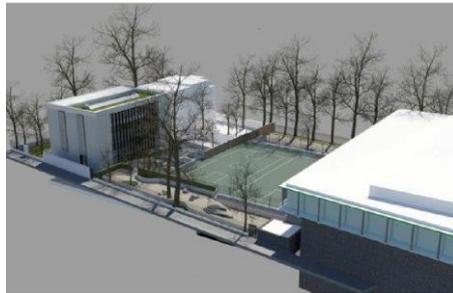

Next 4 Weeks

Over the next 4 weeks we will be progressing with the construction of the concrete frame to the Art Block. The 2nd floor slab, walls & columns are all set to be completed over the next few weeks, along with the construction of the Art Block roof slab.

The concrete structure works to the fitness and dance area will be continued, with the walls, columns & reinforced slab being constructed

The swimming pool structure is set to advance over the next few weeks, with the columns, walls and pool slab works all set to take place over this period.



Community

ISG is a considerate contractor dedicated to its community and as part of its commitment strives to integrate with the surrounding society.



Mirna Ayoubi (Assistant Design Manager) and George Hirons (Placement Trainee) conducted two presentations to the American school students during their assemblies on behalf of our ISG site team. The presentations focused on promoting the construction industry, and informing the students of the progress of works through highlighting similarities between Lego construction and the works taking place on site. Their presentation also gave an insight to the machinery used on site with interesting facts and comparisons to give the students an idea of the scale of works involved, with questions at the end.



The first presentation was presented to 450 Lower School students, aged 4-10. The second presentation was presented to 450 Middle School students, aged 10-14. The presentations were an overall success, praised by Payson Bullard at American School London -



"I wanted to let you know that George Hirons and Mirna Ayoubi did a fantastic job of presenting to our middle school students at ASL last week. The professionals from ISG were informative, engaging and wholly accommodating with regard to our unique needs as an international school here in London. Our teachers and students gave a lot of positive feedback on their presentation. Thank you for the opportunity for our students to meet with George and Mirna."

Payson Bullard | Middle School Coordinator of Student Life | American School in London



Interesting Facts

We have worked **115,240** man hours on site since June 2014.

There have been **NO** reportable accidents or incidents on site since we commenced our works.



There has been approximately **28,345** tonnes of earth removed from site.

Since works commenced on site there has been approximately **1596** vehicle movements to and from site.

In our last Considerate Constructor's audit we received an excellent score of **41 / 50**.

Spotlight on Mirna Ayoubi



My name is Mirna Ayoubi and I am Assistant Design Manager on the project.

I graduated in July 2013 and joined ISG since. I studied Architectural Engineering and Design Management at Loughborough University.

I've always been interested in construction especially in the design aspect of it. ASL is the first construction project I have been involved in and observing its construction and day to day transformation has been such an eye opener.



During my time on site I have been involved in assisting the senior design manager on site first hand and learning new skills a design manager requires. I have also been given the opportunity to shadow the construction managers on site which gave me a much wider understanding of their role on the project. The best part of being a design manager is the ability to work and coordinate with so many professionals such as architects, engineers, subcontractors and more.

It is extremely rewarding observing and being involved in such a large project and I hope ASL will be the first of many construction projects I will get to work on in the future.



Please feel free to call the number highlighted below if there are any issues you wish to discuss and we will endeavour to address these as quickly as possible.

Site Phone Number:

0207 7482664

Senior Project Manager
Eamon Rafferty

Senior Construction Manager

Derek Haran

Assistant Construction Manager
Marius Skrabulis
